Recent and Current Projects

Academic and Athletics Projects

Hormel-Nguyen Intercultural Center

Project Description: Create additional program space on the roof terrace. Completed summer 2021.

Lamb-Miller Field House

Project Description: Roof replacement.

Schedule: Flat roofs and the barrel roof were completed in

July. The skylights will be replaced this fall.

Lang Music Building

Project Description: Heating and air conditioning system upgrades, renovations to restrooms and Presser Room, organ refurbishment, interior accessible ramp to Lang Concert Hall.

Schedule: Completed summer 2021.







Recent and Current Projects

McCabe Library

Project Description: Create LibLAB on main floor as a collaborative student work space, with convenient access to library staff support.

Schedule: Completed summer 2020.

Pearson Hall

Project Description: Heating and air conditioning system upgrades,

building envelope improvements, partial interior renovation.

Schedule: Completion in early September.


Singer Hall

Project Description: New interdisciplinary home for the Biology,

Engineering and Psychology departments.

Schedule: Construction is nearly complete. All spaces will be available

for use for the fall semester.

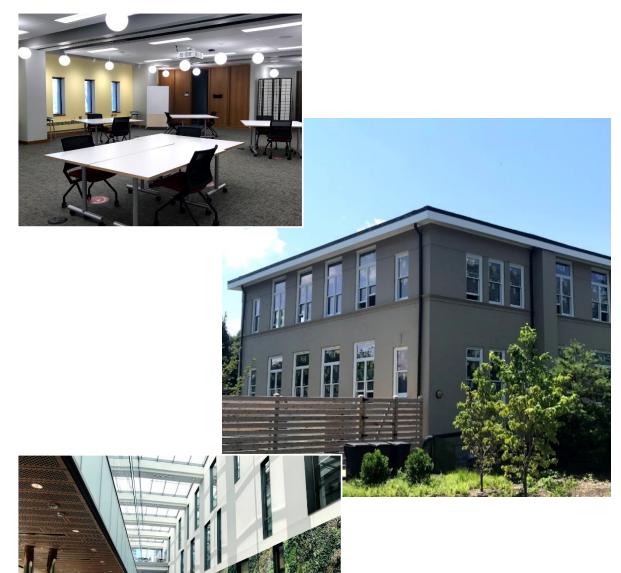

Recent and Current Projects

Whittier Hall

Project Description: Interior renovation to accommodate Art Department faculty studios and senior studios and the ITS Makerspace. Schedule: The senior studios and makerspace will be completed in October; the remaining construction will be completed in January 2022.

Student Services

Dining and Community Commons

Project Description: New dining center and community space; repurposing of Sharples Dining Hall for student and community services. Schedule: The new dining center will open for the fall semester 2022; renovated spaces in Sharples will open for the fall semester 2023.

Kyle House

Project Description: Refurbish commons spaces and exterior; restore to use as student housing.

Schedule: Completed summer 2021.







Recent and Current Projects

Mertz Residence Hall

Project Description: Last phase of a three-year project. Interior renovation of student rooms, bathrooms, common areas; entrance improvements.

Schedule: Most of the work is complete. The entrance doors will be replaced and the elevator will be upgraded later this year.



Upcoming Projects

Academic and Athletics Projects

Clothier Field and Skallerup Track

Project Description: Lighting upgrades for Clothier Field; infield replacement; complete rebuilding of Skallerup Track.

Schedule: Construction is anticipated in 2022, pending

funding approval.

Lamb-Miller Field House/Tarble Pavilion

Project Description: Interior renovation and upgrades for locker rooms, equipment storage and administrative areas.


Schedule: Construction is anticipated in 2022, pending

funding approval.

Martin Hall

Project Description: Repurposing to house the Film & Media Studies and Computer Science departments, along with the ITS Media Center.

Schedule: Design is underway. Groundbreaking is not yet scheduled.







Upcoming Projects

Student Services

Parrish Hall, 3rd & 4th Floors East

Project Description: Central air conditioning, heating system

upgrade, and interior renovation.

Schedule: Construction is anticipated in summer 2022.

Willets Residence Hall

Project Description: Renovation of the bathrooms on the lower level; relocation and expansion of Mephistos kitchen.

Schedule: Construction is anticipated in Summer 2022,

pending funding approval.



Upcoming Projects

Energy Plan Implementation

Standby Electrical Generation Plant


Project Description: Stand-alone plant to reduce the College's dependence on the local utility provider for consistent electrical power.


Schedule: Construction is anticipated to begin in late winter.

The plant will be completed in fall 2022.

Geoexchange Plant and Well Field, Phase 1

Project Description: Central plant and associated well field under Parrish Lawn to provide carbon-neutral heating and cooling to buildings currently served by the steam plant. Schedule: The plant will be located in the basement of the new dining center. Equipment design is underway; design of the well field will begin in early 2022.

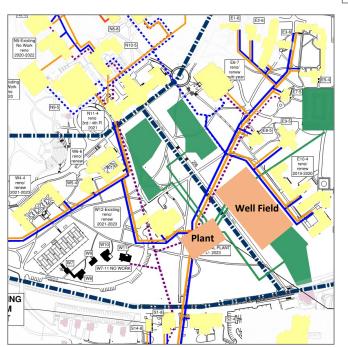

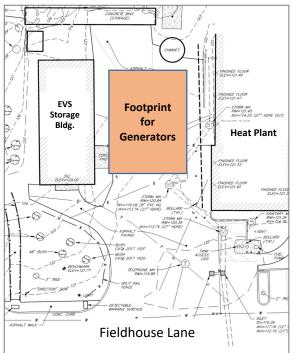

Upcoming Projects

Geoexchange Plant Distribution System: Service to Parrish Hall and North Quad Buildings

Project Description: Installation of main piping from to the north campus; replacement/upgrading of underground utilities around Parrish Hall.

Schedule: Construction is anticipated to begin in summer 2022.

